




Reimagine PJEFC Congregation Update

10 May 2026

Project Management & Governance Structure

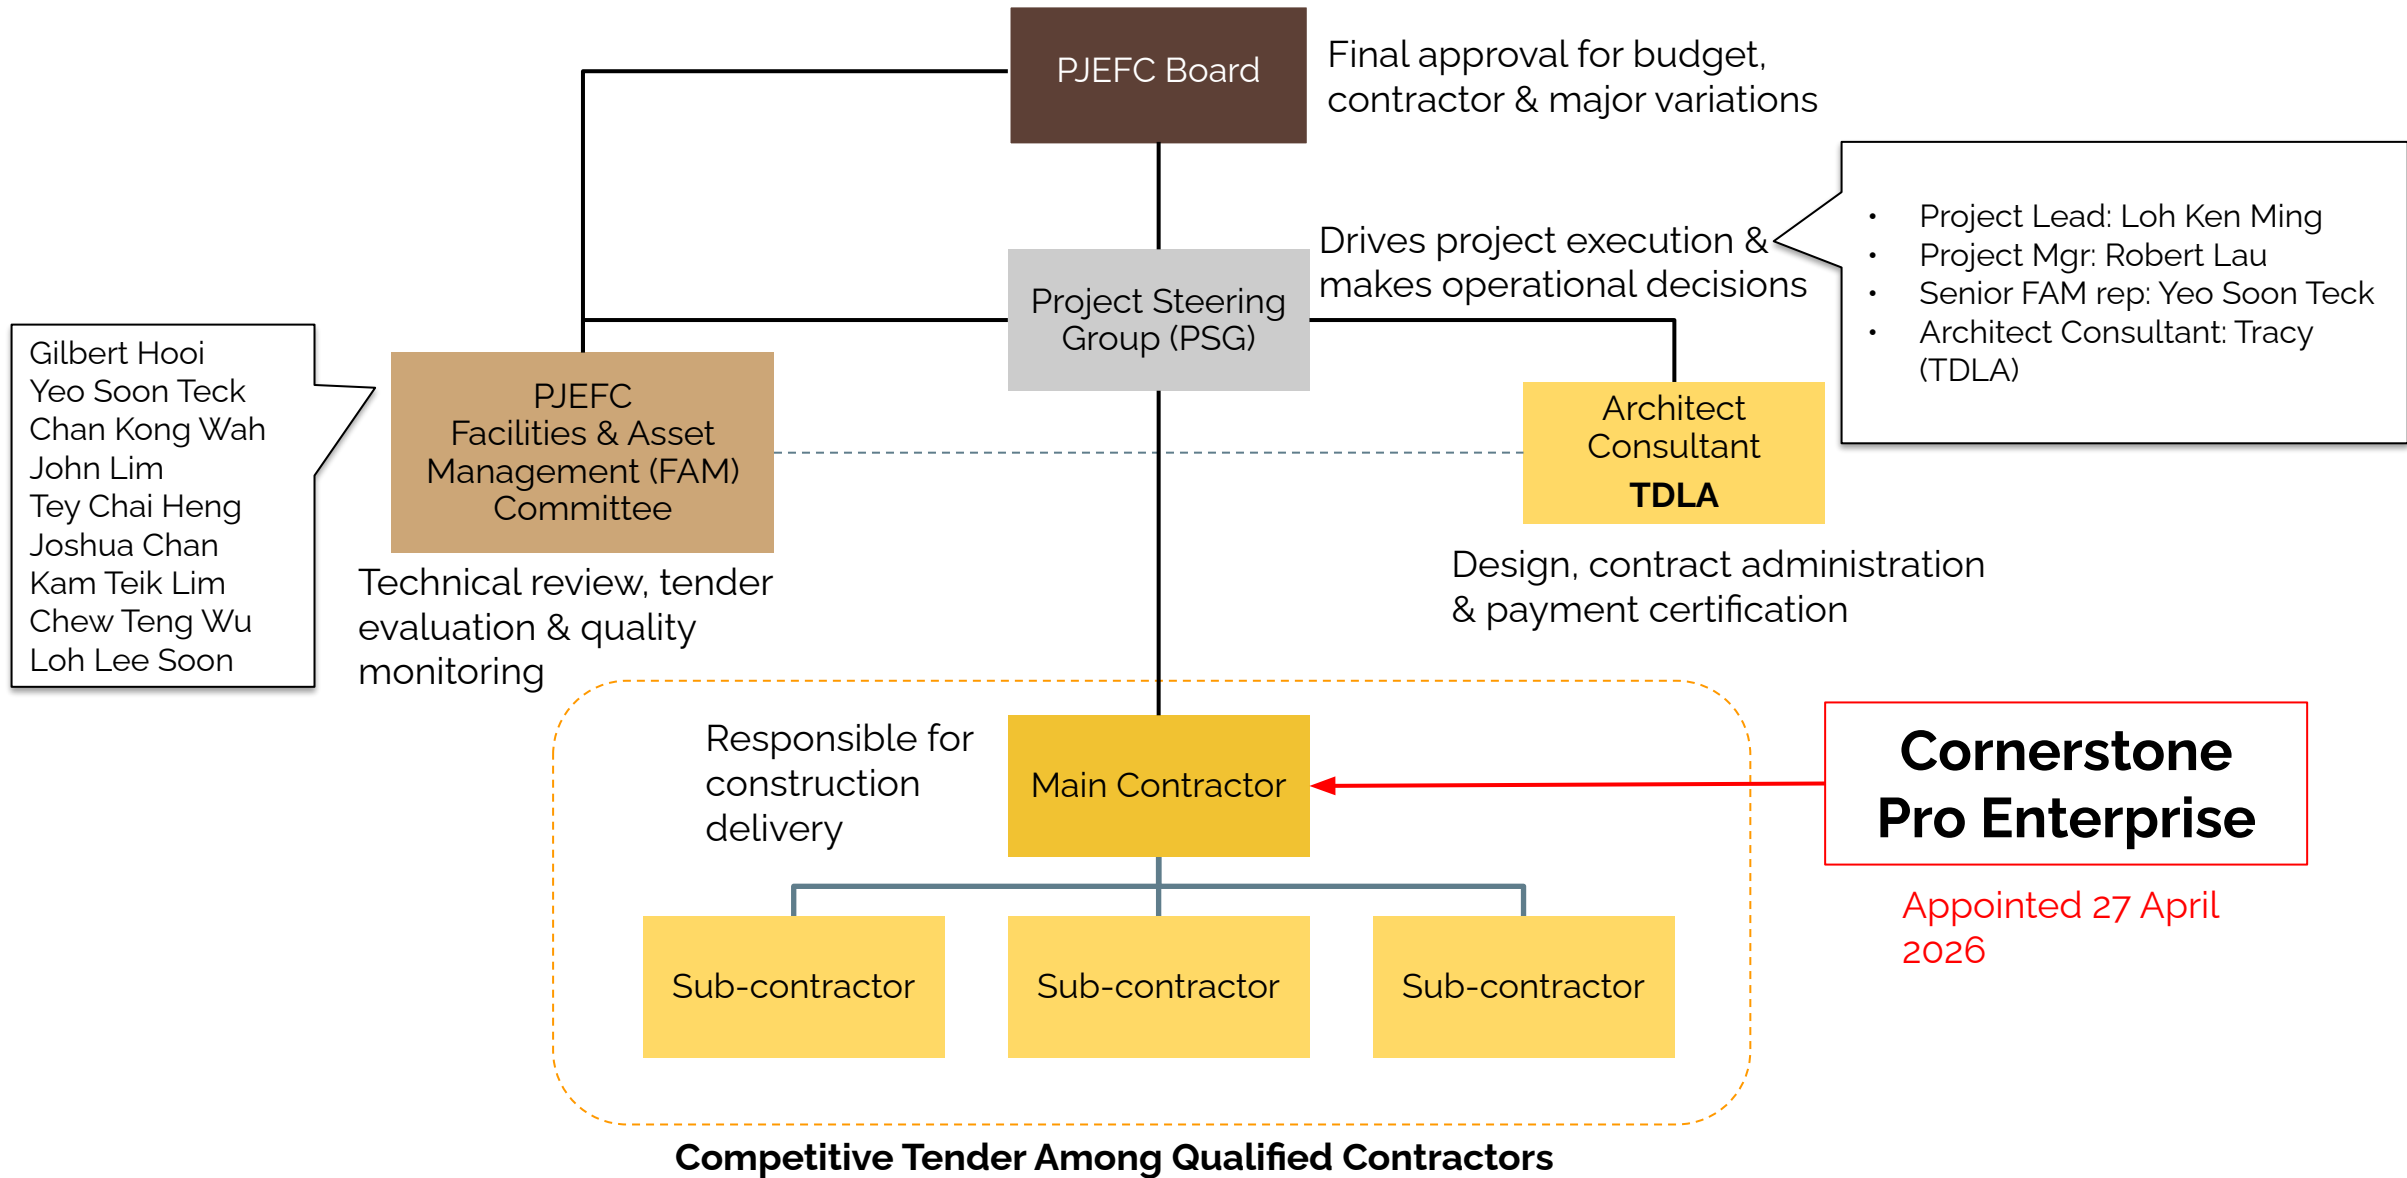


Basement Carpark

Fire Sprinkler installation

Sports complex 1
month closure
11 May – 15 June




FIRE SAFETY	Sprinkler	Hose Reel	Fire Alarm	Testing
LG Carpark	95%	0%	0%	0%
G Concourse/ Auditorium	Plan start mid June			
L2 Sports Complex	10%	0%	0%	0%

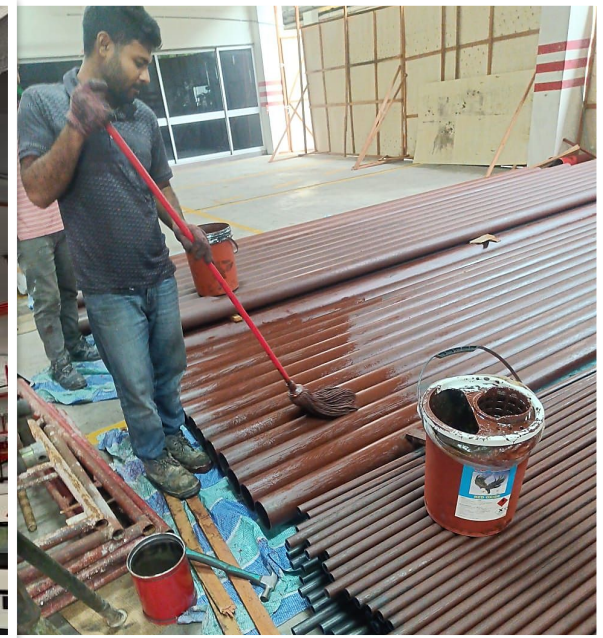

Main Auditorium

Protection & Dismantling works

AUDITORIUM	Preparation, Protection	Remove tarpaulin, lights	Catwalk	Acoustics & Lighting	Sound System
	100%	100%			

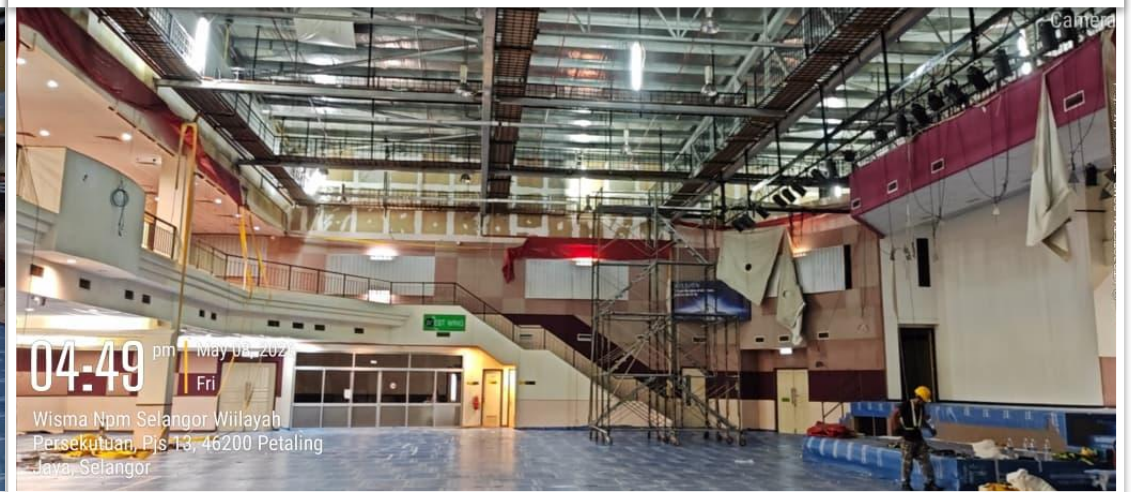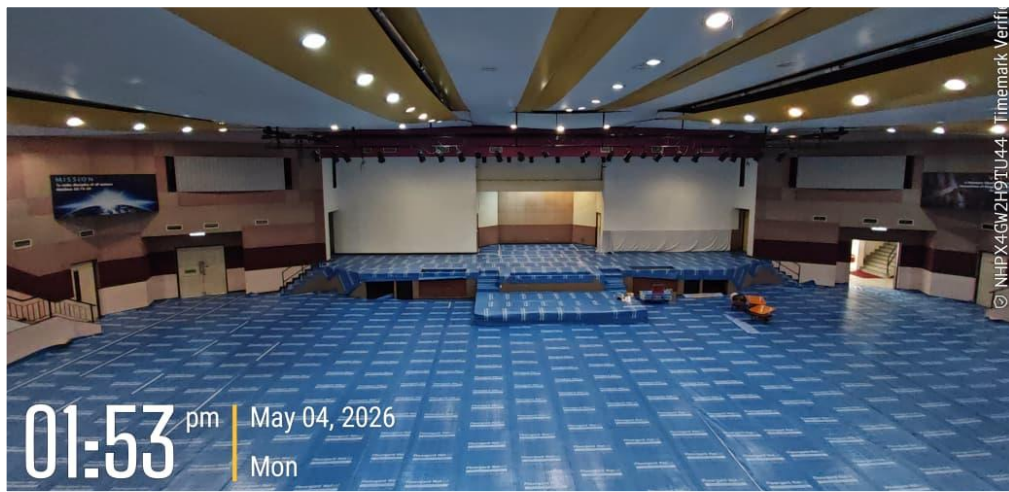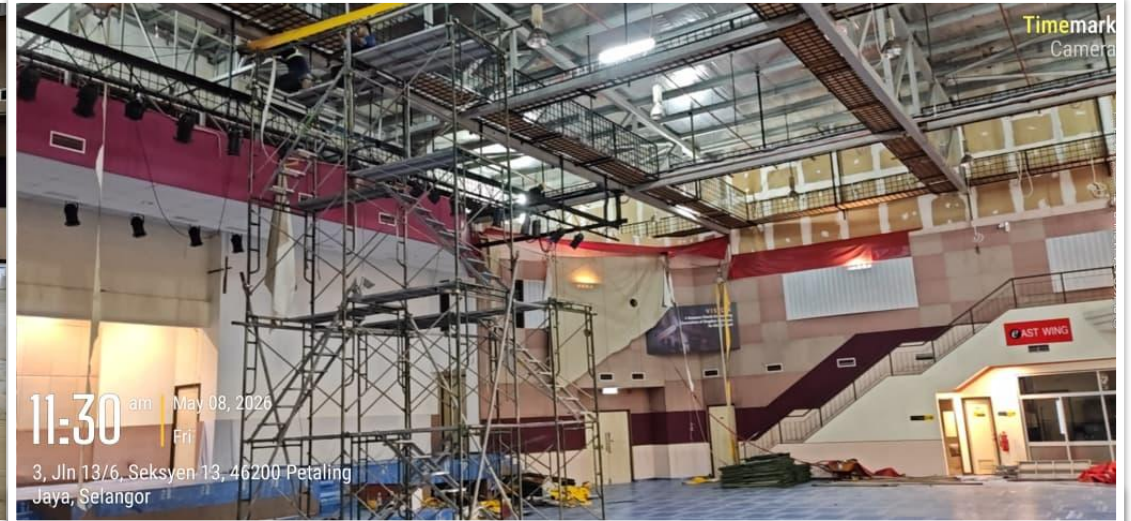

Reimagine: Renovation Timeline 2026

Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	November
-----	-----	-----	-----	-----	-----	-----	-----	----------




CONCOURSE & ENTRY	Demolition	Replace Flooring	Rebuild	ID & Carpentry	Acoustics & Lighting	Painting
CONCOURSE	✓	✓	✓	✓	✓	✓
KOPITIAM / PANTRY	✓	✓	✓	✓	✓	✓
KIDS' PLAY AREA	✓	✓		✓	✓	
VISITOR'S LOUNGE	✓		✓	✓	✓	✓
TOILETS	✓	✓	✓	✓		✓
BLOCK B ENTRANCE		✓				✓

✓
in-scope


Next steps:

1. Main contractor obtain license to begin demolition works
2. Fire Safety works to begin in Sports Complex
3. Finalize Design and appoint vendor Carpentry, Acoustic Treatment, and Flooring

Proposed New Library Space

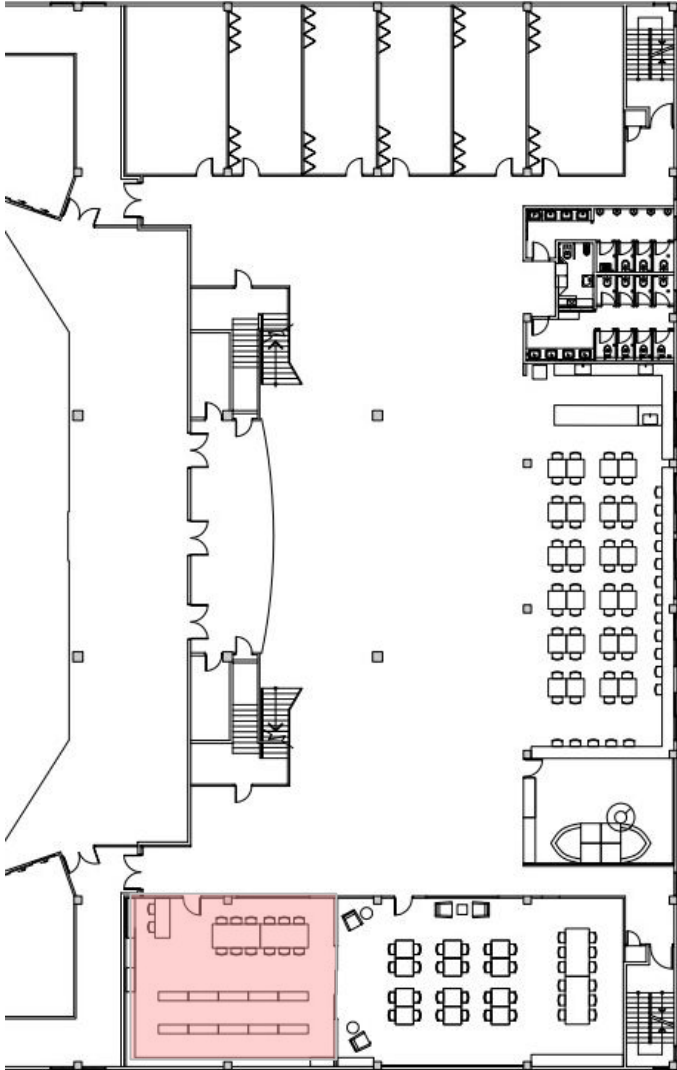

Proposed New Lounge for Visitors & Events

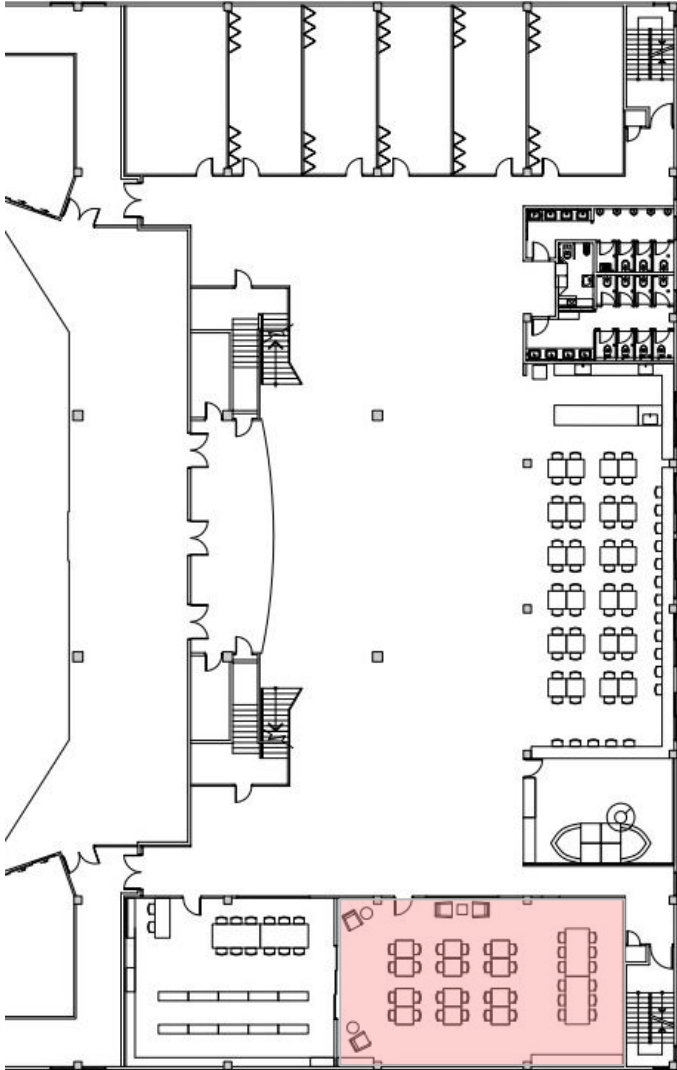

Internal

Budget & Giving @7th May 2026

66.5%

78%


100%

RM 1,993,435 collected

RM2,341,035 pledged

RM3,000,000

Target Project Budget

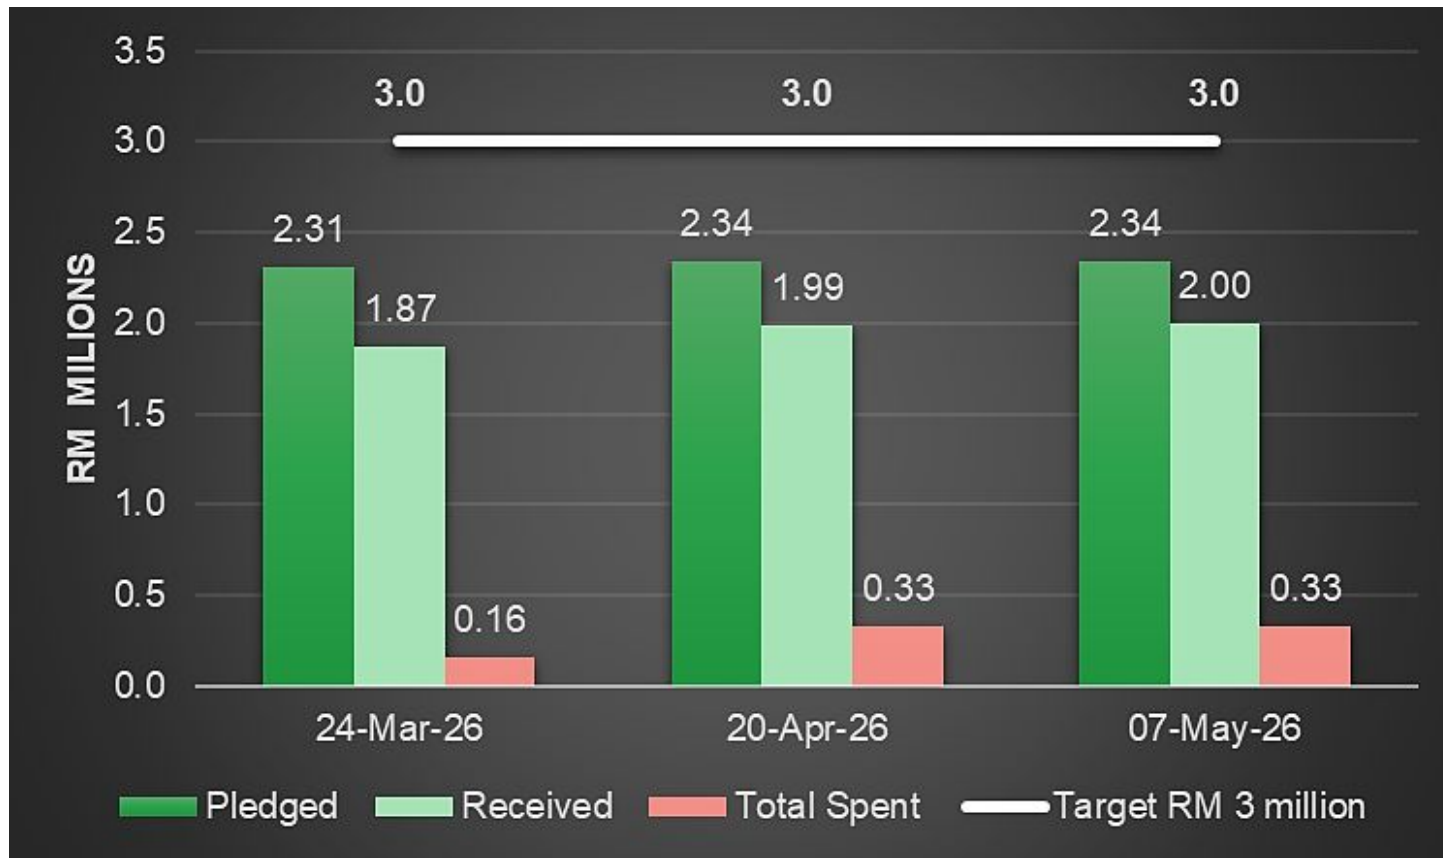

Expenditure is expected to increase significantly within the next few months

Pledge and donate here



<https://tinyurl.com/PJEFCPledge>

Prayer Points for Reimagine PJEFC

Praise

1. Successfully completed Tender and appointed Main Contractor
2. Strong commitment and engagement from FAM and Project Steering committee in moving key decisions
3. Many Consultant and contractors engaged are Christian thus able to provide affordable rates and more understanding of our ministries and space

Prayer

1. Documentation delays to kickstart major works - pray for ways for work to progress quicker
2. Finalize design and appoint sub-contractors - Acoustics, Lighting, Carpentry, Vinyl Flooring
3. Stronger coordination between PJEFC, Consultants, and Contractors
4. Pray for continuous safety and protection for everyone on our premise
5. Fundraising the budget deficit of RM660k to ensure successful completion of the renovation
